



Playable Spaces

Economy and Neighbourhoods Scrutiny Panel

7th April 2022



Playable Spaces

A 5-year, £9.5m programme to improve outdoor play across Kirklees

Our vision is a district where all are able and encouraged to access a range of opportunities to play outdoors, benefitting their physical and mental health and well-being as well as encouraging intergenerational interaction and community cohesion




The journey so far...



2019




2020



Winner of Street Design Award for Manor Rise

2021

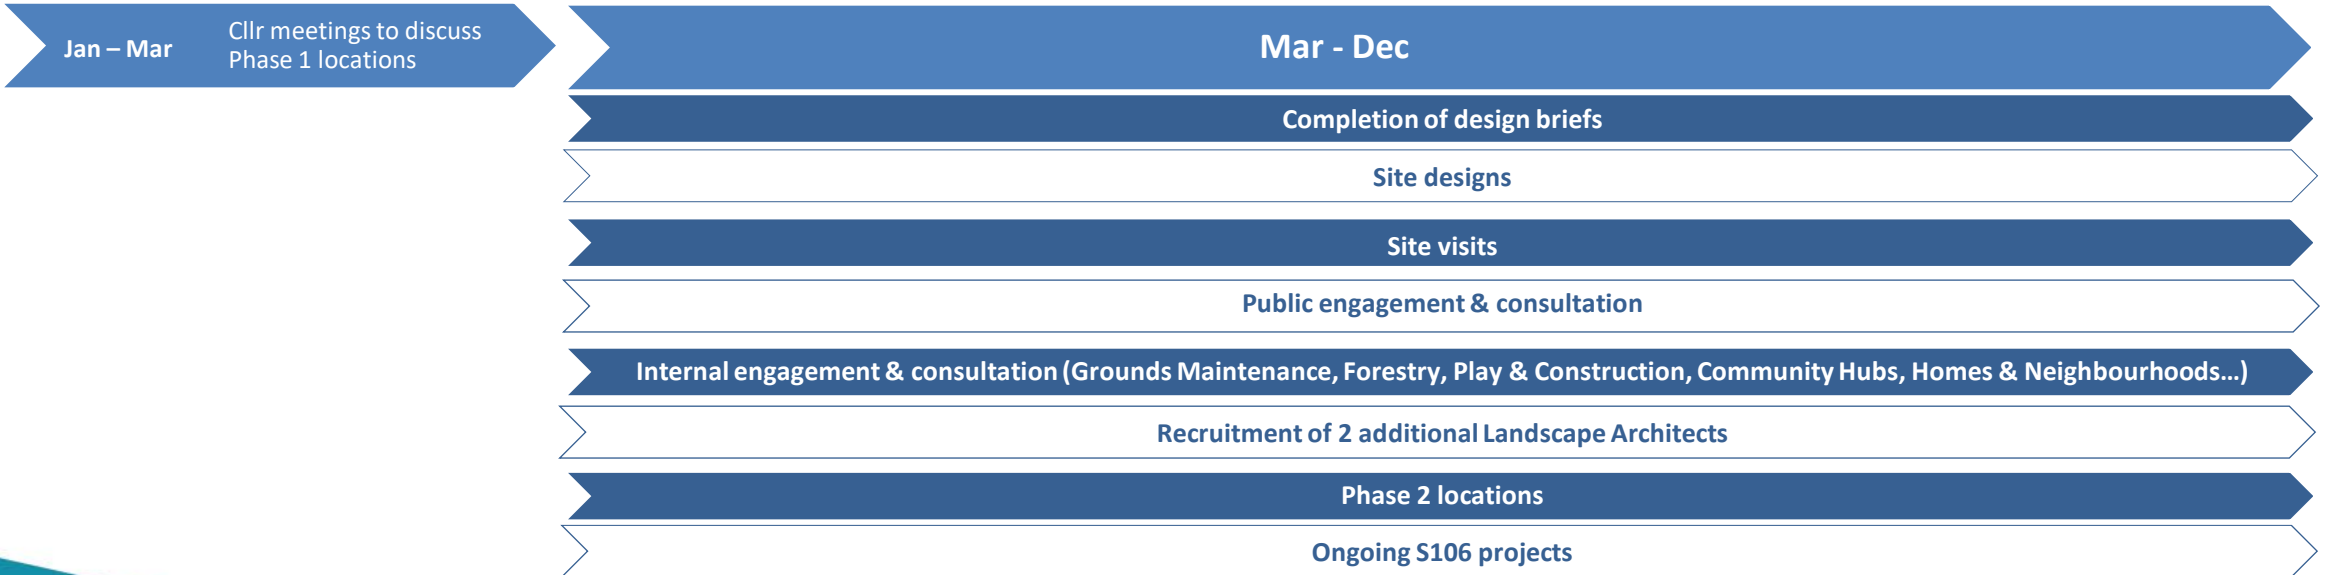

What we have achieved



- Manor Rise, Newsome

Special Judge's Award in the Children's Play category of the 2020 Street Design Awards.



Manor Rise, Newsome



- Branding created and website developed with online district-wide engagement & consultation

Playable Spaces

People, Places & Play

Have your say on play!
We're providing spaces that enable communities to access a range of play opportunities and enjoy the great outdoors.

Causeway Crescent Play Area, Linthwaite

Visit kirklees.gov.uk/playablespaces to complete our online survey, or scan me...
You can also call us on 01484 221000 (ext. 70568)

Kirklees COUNCIL

Engagement

We're starting a rolling plan to engage with local communities on a site-by-site basis to make sure improvements meet the needs of the community.

Due to the number of play spaces we manage, we may not be asking for comments about every site or our approach to engagement, may be limited to the following sites:

- [Arlington Way play area](#)
- [Battye Street play area](#)
- [Causeway Crescent, Linthwaite](#)
- [Haywood Avenue](#)
- [Honley People's Park and Jaggars Lane Recreation Ground](#)
- [Lepton Recreation Ground](#)
- [Primrose Hill Play Area, Primrose Hill](#)

www.kirklees.gov.uk/playablespaces

Planning and development

Home > Leisure and culture > Countryside, parks and open spaces > Playable spaces

Playable spaces

No matter what your age, outdoor activities and play supports our social development, boosts our physical and mental health and brings us closer to nature. Never has this been more noticeable than during the Covid pandemic when many of us made the most of our local outdoor playable spaces.

Play, in its many different forms, is an essential element of helping children to have the best start in life and supporting people of all ages to live as well as possible, for as long as possible. Our Playable Spaces Strategy, created in partnership with Public Health, builds on knowledge and previous public feedback to address some of the barriers to play to help us instil lifelong habits of physical activity and wellbeing.

Engagement
Starting a rolling plan to engage with local communities about play areas on a site-by-site basis.

Social media
 Facebook: Kirklees parks and green spaces
 Twitter: @KirkleesCouncil

Playable spaces
Parks and playgrounds

Leisure and culture
 Oakwell Hall
 Town halls events and tickets
 Libraries online resources
 > More in leisure and culture



Engagement process developed with central Engagement team to support analysis...

...results adopted into designs where practicable and uploaded to website



Kirklees Council
Playable Spaces
 People, Places & Play Survey

Results
 Report on the findings from the survey conducted during the consultation period from 20th July to 31st August 2021.

Summary
 A summary of results for each question as it appeared in the survey is detailed below. Please note percentages may not always add up to 100% due to rounding.

Headline Results

- The majority of respondents (89%) agreed to some extent with the proposals for the redesigned park (56% Yes / 33% Mostly) with 7% not in full agreement.
- The design feature to generate the highest concern was the proposed sheltered seating area. People were worried that it would attract vandalism, littering and anti-social behaviour from teenagers and groups. 17% of participants selected the angry or sad emoji response when asked if they approved of this feature.
- The most popular suggestion was to include a larger, fenced-in playing court including a netball/basketball hoop that could also be used for multiple different sports. The proposed ball court area is considered too small and more for younger children.
- Other popular suggestions included a skate park and picnic tables.
- The sheltered seating area was the most controversial, with 15% of respondents disagreeing to some extent with the proposal.

Do you generally agree with the proposed plan?
 Yes (15) 58%
 Mostly (9) 33%
 Not really (2) 7%
 No (-)
 Not sure / don't know (-)

Are you generally supportive of these proposals? (Phase 1)
 Yes (15) 58%
 Mostly (9) 33%
 Not really (2) 7%
 No (-)
 Not sure / don't know (-)

Do you have any specific concerns about the play area renovations?
 There were 22 comments received on this question.

- The majority of respondents commented that they had no concerns.
- General safety concerns were the second biggest theme.
- The drainage issues at the park were also mentioned by two respondents.

Please use the space below to provide any other comments about these proposals:
 There were 33 comments received on this question.

- The majority of comments were positive and in full support of the proposals.
- Several comments reiterated concerns over safety, drainage and ensuring the park was properly maintained.
- Extra equipment, especially for younger children was also mentioned several times.

Get involved

Thank you to all those who commented on the initial proposals. This consultation is now closed and the project will proceed to delivery phase.

We had 34 responses to the survey which we consider to be a good response rate. The great majority of respondents were generally supportive of both the phase 1 and phase 2 proposals, and all of the features proposed in the phase 1 design. Suggestions for improvements focused primarily on provision for older children and young people.

Whilst it is difficult for us to accommodate this within the budget and space available for the Phase 1 scheme, this will be a focus for Phase 2 developments. This could include more adventurous play equipment for older children, an extension to the footpath which could be used by scooters, and/or static gym equipment. Further consultation will be undertaken prior to the Phase 2 scheme being finalised.

In light of the comments received, we have made some amendments to the designs:

Playable Spaces

Warburton Rec
 Playspace - Sketch Design, Phase 1.


Furniture and Materials Palette

Multiple sites designed with a place based approach

Some phase 1 designs...

Playable Spaces

ARLINGTON WAY- SKETCH PROPOSALS & MOOD BOARD

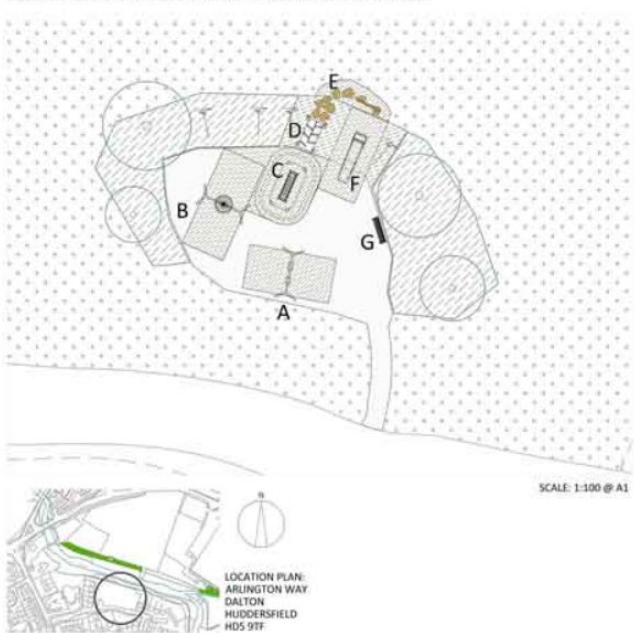

People, Places & Play
kirklees.gov.uk/playablespaces

	A Existing swing refurbished - 1 flat seat, 1 cradle seat		B Sutcliffe Play - Basket Swing		C Playdale - City Suspension Bridge		D Play & Leisure - Embankment Ramp		E Scrambling boulders and log up slope & in level surfacing		F GL Jones - Wide Embankment Slide		G Play & Leisure - Oxford bench
--	--	--	--	--	--	--	---	--	--	--	---	--	--

	Existing trees to be retained
	Existing embankment vegetation
	Existing embankment vegetation to be removed and turfed
	Proposed eco-mulch safety surfacing
	Proposed new tarmac surface over existing
	Existing grass to be retained

SK04-A - KIRKLEES LANDSCAPE ARCHITECTS - SEP 2021

Playable Spaces

People, Places & Play
kirklees.gov.uk/playablespaces


Cemetery Walk, Almondbury



Notes:

This scheme proposes to enhance the existing play area with up-graded play surfacing and repairs to existing play equipment. In addition to this proposed work, additional play equipment is suggested outside the play area; a basket swing (inclusive) and a large climbing. The scheme will also include additional seating, native bulb planting, boundary tree planting and a new relocated mini goal end.



Proposed equipment

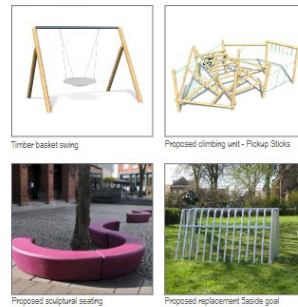

Some phase 1 designs...

Playable Spaces


People, Places & Play
kirklees.gov.uk/playablespaces



Glenfield Avenue

Section of damaged fence to be removed

Area left open for football



THORNCLEIFE ROAD

ASHCROFT CLOSE

Multi play in steel
wobble beam in steel
Burma bridge in steel

Picnic table
Natural stepping stones
Natural boulders
Weave posts

SCALE 1:100 @A1

PLAY STRATEGY : ASHCROFT CLOSE, STAINCLIFFE. Kirklees COUNCIL



Some phase 1 designs...



Playable Spaces

People, Places & Play
kirklees.gov.uk/playablespaces

1 Proposed grass mound with sleeper turret/lookout, embankment slide, scramble net, stepping logs and inclined balance beam. Rubber grass mat around play elements.

2 Proposed 2 bay swing with 2 flat seats, 1 cradle seat & 1 inclusive boat seat. Swing on rubber grass mat.

3 Timber monkey bars, on rubber grass mat.

4 Liquidamber tree

5 New bin and bench

6 Existing concrete foundations broken out
Existing bench refurbished
New picnic bench

7 Alternating avenue of cherry & maple (Prunus padus 'Watereri' & Acer rubrum 'Red Sunset')

Existing trees to remain

Existing trees to remain

Marten Drive Play Area

Feb 2022 SK01 Rev F
Revisions following consultation feedback

Playable Spaces

People, Places & Play
kirklees.gov.uk/playablespaces

Warburton Rec Playspace - Sketch Design, Phase 1.

1 Wokazed Multi-unit - Dinosaurs
System

2 Kompan - forest swing

3 Kompan - butterfly sensor

4 Double swing unit - 4 bay

5 Kompan - forest like boat

6 Sixlife Inclusive Roundabout

Area identified for further play features (see age ranges at the opportunity).

Line markings to new infrastructure track. The could be extended to other games.

Notes:
The play equipment for this scheme has been selected to provide 'more alternative play in particular through older age groups'. A basket swing and roundabout provide accessible play for older children. A limited budget means options for surfacing are constrained therefore it is suggested that the existing tarmac footpath is repaved along with the existing timber round edging. A self-closing gate is proposed to provide an additional barrier to the road. The proposal looks at the option of removing the existing birds round rail on the mound to allow the future to be incorporated into the play area as an additional play element. Natural elements, a boulder and a carved timber feature as enclosed, add play value and interest. Soft low maintenance planting is known to enhance the boundaries of the play area and add another layer of natural play to the scheme. Imaginative play is also encouraged in the design, a timber boat offers the opportunity for all age ranges to role play, for their imaginations to go and enjoy more non-prescriptive play opportunities. The bike track would have new markings to provide a more interesting circular route. Tree planting would add further structure and some shade. A new picnic bench would replace the existing benches.

Furniture and Materials Palette

- Green roof
- 3.5m high tree-like fence
- Tree Planting - Silver Birch
- Soft sand carpet
- Grass (mown/flat)
- Low maintenance planting
- Accessible picnic bench
- Soft play

Further opportunities

- Introduction of additional nature play features.
- Community involvement with wildlife surveys or planting projects.
- High shading on walls or walls.

LOCATION PLAN

Word Docx Date: [blank]
Site Address: Warburton, Embsay, Leeds/Warburton, HD8 3GP

Kirklees
EQUIPMENT SERVICES
RECREATION/PLAY AREAS

DATE: 15/02/2022
FIRST DRAFT FOR COMMENT
SCALE: 1:500
LAD:481 LA:100 6

- Completion of other projects

Beaumont Park



Recent completions

Westerley Way



Recent completions

MUGA at Broadlands Rec



Recent completions

Sycamore Rec



Reporting and Governance



- Fortnightly Project Team meetings and monthly Project & Landscape Architect meetings to review progress and discuss challenges

PLAYABLE SPACES 5 YEAR PROGRAMME																			
SITE INFORMATION																			
Site Name	PDO	LA	Ward	Parent site address	Postcode (either site or closest property to the site)	Original classification	Live PS & other sites	Site Agreement	Engagement option selected 1) full traditional engagement 2) Design->Cllrs->Community 3) Design->Cllrs	Option 1 consultation	Design Brief	Cllr Design Expected	Cllr Design Complete	Design issued to Cllrs for comment	Pre-consultation design complete	Questionnaire Development	Comms checklist complete	Comm engagement complete	
Birkenshaw Bottoms	TJ	EW	Birstall and Birkenshaw	Birkenshaw Lane Recreation Ground, Birkenshaw Lane, Birkenshaw, Bradford	BD11 2EY	Comm	Cllr choice launch site - first site(s) selected by Cllrs due to	Cllr choice	2	n/a	Complete	Complete	Complete	Complete	Complete	Complete	Complete	Complete	Complete
Birkenshaw Park	TJ	HP	Birstall and Birkenshaw	Birkenshaw Park, Bradford Road, Birkenshaw, Bradford	BD11 2AD	Comm	Live S106	With Birkenshaw Bottoms	3	n/a	Complete	Complete	Complete	Complete	Complete	Complete	Complete	Complete	Complete
Broadlands Rec	AM	LC	Holme Valley North	Broadland Recreation Ground, Broadlands Road, Meltham, Holmfirth	HD9 5QY	Comm	Live S106 only	Complete	Complete	Complete	Phase 1 - C Phase 2 - C	Phase 1 - C Phase 2 - C	Phase 1 - C Phase 2 - C	Phase 1 - C Phase 2 - C	Phase 1 - C Phase 2 - C	Phase 1 - C Phase 2 - C	Phase 1 - C Phase 2 - C	Phase 1 - C Phase 2 - C	Phase 1 - C Phase 2 - C
Bywell Play Area	RP	HP	Dewsbury East	Open Space, Leeds Road, Dewsbury	WF12 7QE	Comm	Live S106/PS project	Agreed	2	n/a	Complete	In progress							
Causeway Crescent	AM	HP	Colne Valley	Causeway Crescent Recreation Ground, Causeway Crescent, Linthwaite, Huddersfield	HD7 5NN	Comm	Cllr choice launch site	Cllr choice	2	n/a	Complete	Complete	Complete	Complete	Complete	Complete	Complete	Complete	Complete
Cemetery Walk	TJ	AR	Almondbury	Almondbury Recreation Ground, Cemetery Road, Almondbury, Huddersfield	HD5 8XD	Comm	Cllr agreed launch site	Site 1 agreed	2	n/a	Complete	Complete	Complete	Complete	Complete	In progress			
Cinderhills Rec	AM	MS	Holme Valley South	Cinderhills Recreation Ground, Field Road, Holmfirth	HD9 1EJ	Comm	Live S106/PS project	Complete	Complete	Complete	Complete	Complete	Complete	Complete	Complete	Complete	Complete	Complete	Complete
Crow Lane	AM	EW	Golcar	Crow Lane Recreation Ground, Crow Lane, Milnsbridge, Huddersfield	HD3 4QT	Comm	Cllr agreed launch site	Site 1 agreed	2	n/a	Complete	In progress							
Crow Nest Park	RP		Dewsbury West	Crow Nest Park, Heckmondwike Road, Dewsbury Moor, Dewsbury	WF13 2LW	Dest	2nd site for DW	Agreed	1	Survey to be developed									
Earlsheaton Park	RP	HP	Dewsbury East	Earlsheaton Park, Cross Park Street, Earlsheaton, Dewsbury	WF12 8JG	Dest	Live S106/PS project	Agreed	2	n/a	Complete	In progress							

Extract from programme tracker

- Feeding into the Parks & Greenspaces reporting governance structure

Implementation Group > Management Group > Transformation Board




Monthly Portfolio Lead Report

Status update – Playable Spaces, 25/02/2022

Outcome – to deliver a mixed play portfolio of traditional, adventurous and imaginative play using both play equipment and natural features – with this play portfolio meeting the needs of all within our communities

Project RAG AMBER	Complete	On track	Subject to re-planning	May slip with material impact
-------------------	----------	----------	------------------------	-------------------------------

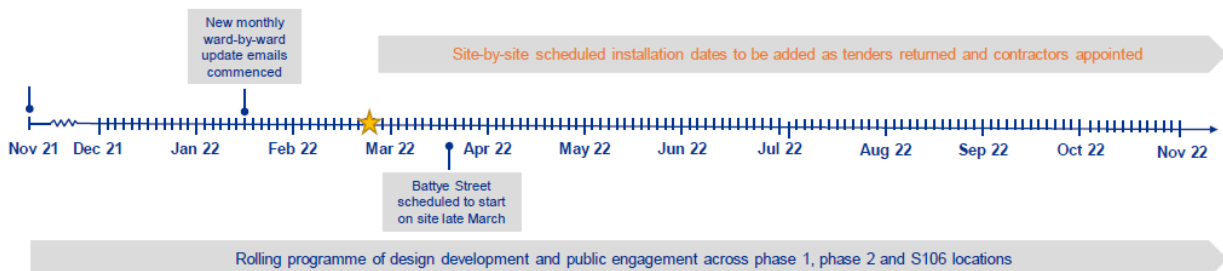

Summary – Phase 1 Sites

Summary	23/02/2022
Design process	2
Approval process (internal teams and Cllrs)	7
Public engagement (with design)	1
Design amendments, technical design, tender documentation	9
Procurement process	2
Contractor appointment and enabling works	1
On site	0
On hold (Lee Street - underground cellar investigations)	1

Key risks and (mitigation)

- Capacity and impact on timeline
- We are losing a PDO, therefore sites remain split between PDO's, Project Officer, Prog Manager and Parks Services Manager
- Procurement DPS system
- There is still a backlog as issues are ironed out with this central system, but the team are catching up



Any issues to report

- Tender return pricing
- Due to inflated costs being seen across the industry, tender returns are coming in high, taking us over budget. This has been highlighted at the Parks & Greenspaces Management meeting with WA and a new Transformation Board with CP. Senior managers are in agreement that whilst we are seeing inflated costs we will sink these and report on Phase 1 overspend to analyse future requirements.

Activities completed last period & underway

- Monthly reports for February issued – these updates are proving popular with ward members
 - Contractor appointed for Battye Street
- ### Activities due next period
- Battye Street works due to start on site late March 2022

Item	Last period	Current period	Trend
Schedule	Amber	Amber	➡
Resourcing	Amber	Amber	➡
Stakeholders	Green	Green	➡
Outcomes	Green	Green	➡

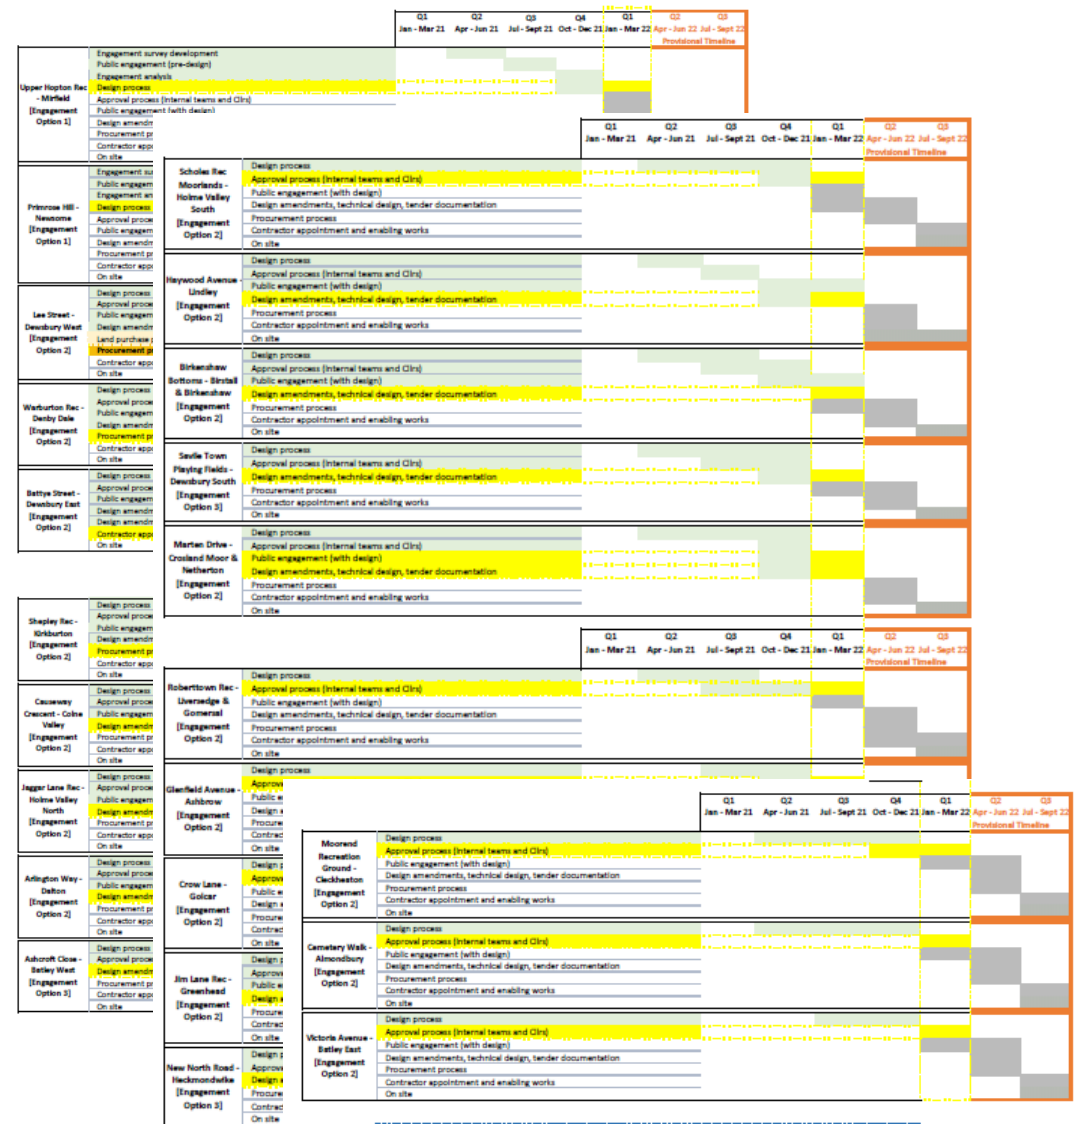

Summary – Phase 2 sites & S106 projects

We are in various stages of bringing the next sites on board:

- Lepton Rec, Almondbury
- Rectory Park, Dewsbury South
- Staincliffe Park, Batley West
- Grange Moor Park & Rec, Kirkburton
- Crow Nest Park, Dewsbury West
- Sunnymead, Denby Dale

Across the various play projects within the team we have just short of 50 sites in different stages of development

Summary	23/02/2022	24/02/2022	26/02/2022	28/02/2022	01/03/2022
Design process	2	2	4	9	
Approval process (internal teams and Cllrs)	7	6	5	6	
Public engagement (with design)	1	3	3	2	
Design amendments, technical design, tender documentation	9	6	6	4	
Procurement process	2	3	2	2	
Contractor appointment and enabling works	1	0	0	0	
On site	0	0	0	0	
On hold (Lee Street - underground cellar investigations)	0	0	0	0	



Monthly Councillor Update Reports

From: [Daisy McMurdo](#)
To: [Cllr Charles Graves](#); [Cllr Terry Lyons](#); [Cllr Paul G White](#)
Cc: [Catherine Little](#); [Moira Scarff](#); [Alasdair Menmuir](#); [Louisa Cristobal](#); [Christina Lee](#); [Helen Proudfoot](#)
Subject: Playable Spaces Update - February 2022 - Holme Valley North
Date: 18 February 2022 15:35:29

Good afternoon Cllrs,

I hope you're well.

Following our recent full Playable Spaces team meeting with Parks Development Officers and the Landscape Architect Team, please see below the February 2022 monthly update email to keep you posted on the status of the Playable Spaces and other play area projects within your ward.



Jagger Lane Rec & Honley Peoples Park:

An issue relating to the adjoining PROW at Jagger Lane with a gate in place has been highlighted to us by the internal PROW team. Options to resolve this will be presented to Cllrs as soon as the review of the issue has been completed by officers. We are confident however that we are still able to push forward into procurement of the play scheme despite the ongoing resolution relating to the PROW. Honley Park will go out for tender with Jagger Lane.

Broadlands Rec:

The Phase 1 works are still ongoing on site. There has been a slight slip in programme of 1 week due to the weather. We are now planning the public engagement for Phase 2 works and are on track to go out for consultation in March.

Meltham Pleasure Grounds:

We are at practical completion however the ground is still too wet to install the grass matting. Until the condition improves we will leave the fencing up around the site.

If you have any questions or queries please don't hesitate to get in touch.

Thanks,

Daisy McMurdo
Project Support Officer
Environment & Greenspace
Flint Street, Fartown, Huddersfield, HD1 6LG
Tel: 01484 221000



From: [Daisy McMurdo](#)
To: [Cllr Bill Armer](#); [Cllr Richard Smith](#); [Cllr John Taylor](#)
Cc: [Catherine Little](#); [Moira Scarff](#); [Alasdair Menmuir](#); [Michelle Stevens](#); [Adam Bout](#)
Subject: Playable Spaces Update - February 2022 - Kirkburton
Date: 18 February 2022 15:39:18

Good afternoon Cllrs,

I hope you're well.

Following our recent full Playable Spaces team meeting with Parks Development Officers and the Landscape Architect Team, please see below the February 2022 monthly update email to keep you posted on the status of the Playable Spaces and other play area projects within your ward.



Shepley Rec:

This site will go out to procurement through the DPS system next week with a 2 week return period.

Grange Moor Park & Grange Moor Rec

It has been agreed that these two sites will be the next sites for development as part of the programme. Initial conversations regarding this will be set up by Moira or Alasdair soon.

Highburton Recreation Ground:

Site recently completed and the surplus from the budget will be spent on some small path improvements/maintenance.

Westerley Way:

The fence will be taken down on 17th Feb 2022, and so the playground will be officially complete and open!

Thank you,

Daisy McMurdo
Project Support Officer
Environment & Greenspace
Flint Street, Fartown, Huddersfield, HD1 6LG
Tel: 01484 221000



From: [Catherine Little](#)
To: [Cllr Manisha Kaushik](#); [Cllr Elin Hill](#); [Cllr Mohammad Sarwar](#)
Cc: [Alasdair Menmuir](#); [Daisy McMurdo](#)
Subject: Playable Spaces Update - January 2022 - Crossland Moor & Netherton
Date: 21 January 2022 16:19:00

Good afternoon Cllrs,

I hope you're well.

From this month you will start to receive a monthly update email to keep you posted on the status of the Playable Spaces and other play area projects within your ward. We'll be sending them around the 3-4th week of the month following a full Playable Spaces team meeting that's held with Parks Development Officers and the Landscape Architect Team.



Marten Drive:

Following the responses received from the engagement exercise we have made a number of changes to the scheme. The engagement showed that this space is highly valued and is very much utilised, therefore additional play provision is required. The new plans are currently going through an internal review and we plan to share the final plan with you in the next couple of weeks, prior to sending back out for public review.

Beaumont Park:

This site is complete and is receiving great feedback! The last item to be installed is the main sign welcoming people to the play area. This is in production and installation will be scheduled shortly.



If you have any questions or queries please don't hesitate to get in touch.

Thanks,
Catherine

Catherine Little
Programme Manager
Environment & Greenspace
Flint Street, Fartown, Huddersfield, HD1 6LG
Tel: 01484 221000



Challenges, risks and lessons learnt



Challenges & Risks

- Team Capacity
 - Parks Development Officers – reduced capacity due to vacancy. To mitigate this a more focused approach has been introduced to allow PDOs, the Programme Manager, the Parks Services Manager and our Project Support Officer to concentrate on where their skill set is best used.
 - Landscape Architects – in summer 2021 we recruited 2 new Landscape Architects whose primary focus is Playable Spaces. We're recruiting a further 2 new Landscape Architects this year as more Phase 2 and Phase 3 sites come on board.
- Design Challenges
 - Capacity – as mentioned above our new LAs joined us in the summer and helped to work through the backlog of phase 1 designs.
 - Budget – some of our site specific budgets are tight and designing to meet expectations can be time consuming, however it also leads to creativity and new ideas.
 - Long term maintenance – our strategy encourages nature and more natural elements to be incorporated into our outdoor play spaces. This is a new and different ask and so to mitigate this we are looking to appoint a dedicated Grounds Maintenance Team whose focus will be to maintain the GM aspects of our more natural-style play areas.
 - Accessible play equipment – we are regularly asked to incorporate accessible play equipment into the new designs. We are doing this where budget allows, but when the right location comes on board, we would also like to explore the option of implementing a flagship accessible play area at one of our destination parks.



Delivery Lessons Learnt

External Influences

- Costs and Inflation – inflated costs being seen across the industry are leading to high tender returns which exceed our site budgets. This has been highlighted through our Governance process and senior managers are in agreement that we will absorb these inflated costs in the short term and then report on Phase 1 overspend to analyse future requirements.
- Availability of external contractors – as more sites are going out for tender, we're finding that there are limitations on market capacity. Where this is the case, we're working closely with our Procurement colleagues and also with the contractors to ensure they can meet the required workloads.
- Manufacture and delivery timelines – due to raw material availability and longer delivery times from Europe, lead times are longer than previously experienced, however this is built into the lead-in time to ensure accurate start-on-site dates.

These factors have led us to adapting ways of working and our approach to delivering the programme;

- Site delivery in and out of house – delivery will be split between our internal Play & Construction Team and external contractors
- Procure in batches – to achieve efficiencies external procurement is completed in batches where appropriate
- The S106 programme runs tightly alongside the Playable Spaces programme to ensure resource is managed effectively
- Communication – we appreciate and acknowledge that there can sometimes be long periods of time in between communication with Councillors whilst sites are going through each stage. Therefore, we have introduced our monthly update emails which are being received positively.



Our current programme portfolio



Phase 1 programme timeline: March – June 2022

	March	April	May	June
Upper Hopton	Design	Approvals	Engagement	Amendments/Tech design/tender doc
Primrose Hill	Research	Design	Approvals	Engagement
Lee Street	On hold - underground cellar investigation underway			
Warburton Rec	Technical design/tender	Procurement	Contractor / Enabling	On site (TBC)
Battye Street	Procurement	Contractor / Enabling	On site	
Shepley Rec	Procurement	Contractor / Enabling	On site (TBC)	
Causeway Crescent	Technical design/tender doc	Procurement	Contractor / Enabling	On site (TBC)
Jaggar Lane Rec	Technical design/tender doc	Procurement	Contractor / Enabling	On site (TBC)
Arlington Way	Technical design/tender doc	Procurement	Contractor / Enabling	On site (TBC)
Ashcroft Close	Amendments/Tech design/tender doc	Procurement	Contractor / Enabling	On site
Scholes Rec Moorlands	Approval Process		Engagement	Amendments/Tech design/tender doc
Haywood Avenue	Engagement	Technical design/tender doc	Procurement	Contractor / Enabling
Birkenshaw Bottoms	Amendments/Tech design/tender doc		Procurement	Contractor / Enabling
Savile Town Playing Fields	Amendments/Tech design/tender doc		Procurement	Contractor / Enabling
Marten Drive	Amendments/Tech design/tender doc		Procurement	Contractor / Enabling
Roberttown Rec	Approvals		Engagement	Amendments/Tech design/tender doc
Glenfield Avenue	Approvals		Engagement	Amendments/Tech design/tender doc
Crow Lane	Approvals		Engagement	Amendments/Tech design/tender doc
Jim Lane Rec	Amendments/Tech design/tender doc		Procurement	Contractor / Enabling
New North Road	Amendments/Tech design/tender doc		Procurement	Contractor / Enabling
Moorend Rec	Approval Process		Engagement	Amendments/Tech design/tender doc
Cemetery Walk	Approval Process	Engagement		Amendments/Tech design/tender doc
Victoria Avenue	Design	Approval Process	Engagement	Amendments/Tech

Dates are estimated and can be subject to change

Since 2019 works have been undertaken on 14 play areas across the district



All live projects across Phase 1 & 2, S106 & Trust Fund projects

Norman Park

Arlington Way

Two Furrows Rec

Highburton Rec

Cinderhills

Victoria Avenue

Meltham Pleasure Grounds

Upper Hopton Rec

Birkenshaw Bottoms

Ashcroft Close

Firth Park

Shepley Rec

Jaggarr Lane Rec

Earlsheaton Park

Crow Lane

Roberttown Rec

Honley Park

Cemetery Walk

Lepton Rec

Warburton Rec

Hayward Avenue

Grange Moor Park

Wakefield Road

Beaumont Park

West End Park

Bywell Play Area

Sunnymead

Lee Street

Causeway Crescent

Holroyd Park

Primrose Hill

Netherthong Village

New North Road

Birkenshaw Park

The Oval

Scholes Rec Moorlands

Jim Lane Rec

Rectory Park

Battye Street

Grange Moor Rec

Marten Drive

Broadlands Rec

Glenfield Avenue

Goldington Avenue

Moorend Recreation Ground

Savile Town Playing Fields



Open to questions

